
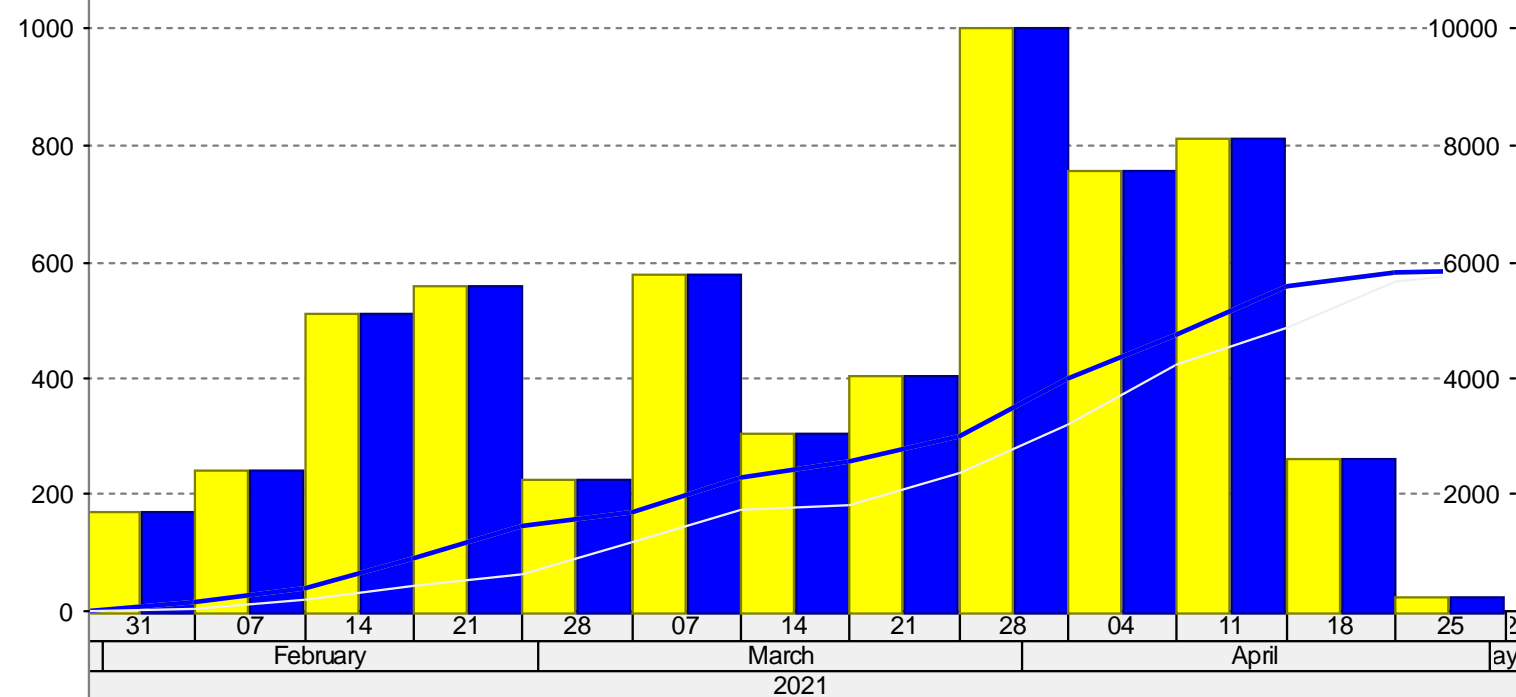






<h1>Construction of 200000 GAL Capacity Water</h1>		<table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>23-Jan-21</td> <td>R-00</td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	23-Jan-21	R-00														
		Date	Revision	Checked	Approved																	
		23-Jan-21	R-00																			

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2021													
						February				March				April				May	
						31	07	14	21	28	07	14	21	28	04	11	18	25	01
📁 Construction of 200000 GAL Capacity Water		61d	01-Feb-21	26-Apr-21	3d	▶ 26-Apr-21													
📁 Preliminary Stage		61d	01-Feb-21	26-Apr-21	3d	▶ 26-Apr-21													
📁 A1000	Project Start	0d	01-Feb-21		3d	◆ Project Start													
📁 A1010	Project Mobilization	1d	01-Feb-21	01-Feb-21	3d	▶ Project Mobilization													
📁 A1020	Primary Works to Start Project	1d	02-Feb-21	02-Feb-21	3d	▶ Primary Works to Start Project													
📁 A1150	Project Finish	0d		26-Apr-21	3d	▶ Project Finish													
📁 Construction Stage		57d	03-Feb-21	22-Apr-21	3d	▶ 22-Apr-21, C													
📁 A1030	Cleaning and Grabing of Site	2d	03-Feb-21	04-Feb-21	3d	▶ Cleaning and Grabing of Site													
📁 A1040	Site Survey Work	1d	04-Feb-21	08-Feb-21	3d	▶ Site Survey Work													
📁 A1050	Excavation Work	2d	08-Feb-21	10-Feb-21	3d	▶ Excavation Work													
📁 A1060	P.C.C Work	3d	10-Feb-21	15-Feb-21	3d	▶ P.C.C Work													
📁 A1070	Raft Foundation Work	16d	15-Feb-21	09-Mar-21	3d	▶ Raft Foundation Work													
📁 A1080	Column Concrete Work	12d	09-Mar-21	25-Mar-21	3d	▶ Column Concrete Work													
📁 A1090	Shear Wall Concrete Work	9d	25-Mar-21	07-Apr-21	3d	▶ Shear Wall Concrete Work													
📁 A1100	MEP Fiting in Walls	1d	07-Apr-21	08-Apr-21	3d	▶ MEP Fiting in Walls													
📁 A1110	Water Tank Slab Concrete	7d	08-Apr-21	19-Apr-21	3d	▶ Water Tank Slab													
📁 A1120	Backfliing Work	3d	19-Apr-21	22-Apr-21	3d	▶ Backfliing W													
📁 Completion Stage		2d	22-Apr-21	26-Apr-21	3d	▶ 26-Apr-21													
📁 A1130	Project Handover	1d	22-Apr-21	23-Apr-21	3d	▶ Project Har													
📁 A1140	Demobilization	1d	23-Apr-21	26-Apr-21	3d	▶ Demobilization													



### Units

-  Budgeted Labor
-  Actual Labor
-  Remaining Labor
-  Remaining Late Labor
